

PROJECTS AT
ANURADHAPURA 2018

NORTHERN REGION UNIT

NORTH CENTRAL PROVINCE

District	Completed projects in 2017	On going projects	New projects
ANURADHAPURA			
	Proposed Recreational Facility Building at Kumbichchankulama	Construction of public Fair at Anuradhapura STAGE 1	Re development of Public Fair at Anuradhapura -STAGE 11
	Resting Park at Mihinthale	Proposed Landscape project around Commercial Building at- Mihinthale	Construction of Market Building at Kekirawa –STAGE 11
	Proposed Bus Stand at Mihinthale	Design and Construction of access road, landscaping & public space Development at Kekirawa	Recreational centre at Kumbichchankulama –(Jogging track continuation)STAGE 111
		Thambuththegame City Centre Development	
		Elayapattuwa town Centre Development	
		Design& construction of service road development at Nochchiyagama	
		Proposed recreational Facilities at Kumbichchankulama - Stage ii	
		Town Centre Development project at Anuradhapura	
	03	08	03

Completed projects at NCP, Anuradhapura

“Sisila Uyana” Recreational Facility Development
project, Kumbichchankulama, Anuradhapura.



Resting Park – Mihintale



Bus Stand Development Project at Mihintale




ON GOING PROJECTS AT ANURADHAPURA DISTRICT

ON GOING PROJECTS AT ANURADHAPURA DISTRICT

PUBLIC FAIR REDEVELOPMENT PROJECT AT ANURADHAPURA –STAGE I

Client	Anuradhapura MC
Contract sum	Rs.180Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date(Stage 1)	September 2017
Completion Date (Stage 1)	March 2018
Allocation for year 2018 (Stage 1)	Rs.43.7Mn
Progress of the Project	<ul style="list-style-type: none">•40% Completed•Block A - 15% completed•Block C & D up to roof level•Block E up to slab level
Cumulative payments to Date	Rs.61Mn
Consultancy fees obtained to date	Rs.0.3Mn

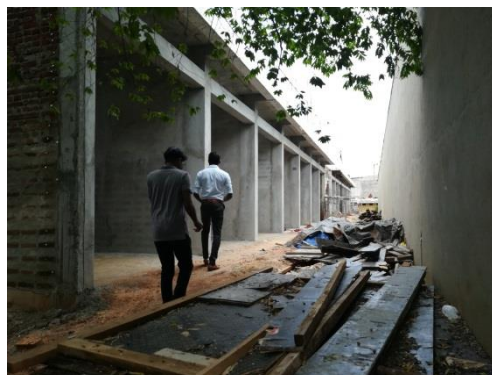

Nine provinces-
Continuation of
balance of the
awarded contract)

Consultancy fees expected
Rs. 0.9Mn

ON GOING PROJECTS AT ANURADHAPURA DISTRICT

MIHINTALE TOWN CENTER REDEVELOPMENT PROJECT

Proposed Commercial Building at Mihinthale

Client	Mihinthale PS	   
Contract sum	Rs.28Mn	
Source of Fund	UDA Treasury	
Commencement date	April 2017	
Completion Date	March 2018	
Allocation for year 2017	Rs.28Mn	Nine provinces- Continuation of balance of the awarded contract)
Progress of the Project	<ul style="list-style-type: none">•98% Completed•Commercial building completed•Service road up to finish level	
Cumulative payments to Date	Rs.26Mn -	
Consultancy fees obtained to date	Rs.0.26Mn	Consultancy fees expected Rs.0.28Mn

ON GOING PROJECTS AT ANURADHAPURA DISTRICT**KEKIRAWA TOWN CENTER DEVELOPMENT PROJECT****- Remedying Defects of existing Market Building**

Client	Kekirawa PS	    <div>Nine provinces- Continuation of balance of the awarded contract)</div>
Contract sum	Rs.50Mn	
Source of Fund	Ministry of Mega Police and Western Development	
Commencement date	June 2017	
Completion Date	March 2018	
Allocation for year 2018 (StageI)	Rs.8.55Mn	
Progress of the Project	80% Completed Finishing works and landscape work ongoing. -Defect of Existing building have to be completed.	
Cumulative payments to Date	Rs.43Mn	
Consultancy fees obtained to date	-Rs. 0.21 Mn	Consultancy fees expected Rs. 0.25 Mn

CITY CENTER REDEVELOPMENT PROJECT- THAMBUTHTHEGAMA

Client	Thalawa PS	<div>Line provinces- continuation of balance of the warded contract)</div> 
Contract sum	Rs.72Mn	
Source of Fund	Ministry of Mega Police and Western Development	
Commencement date	August 2017	
Completion Date	April 2018	
Allocation for year 2018	Rs.25.38Mn	
Progress of the Project	55% Completed Completed up to slab level	
Cumulative payments to Date	Rs.16Mn	
Consultancy fees obtained to date	Rs.0.08Mn	Consultancy fees expected Rs.0.36 Mn

ELAYAPATHTHUWA TOWN IMPROVEMENT PROJECT

Client	Kekirawa PS
Contract sum	Rs.43.5Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date	August 2017
Completion Date	February 2018
Allocation for year 2018	Rs.16.29Mn
Progress of the Project	60% Completed <ul style="list-style-type: none">•Construction of drain up to top level•Walking path 65% completed•Parking 70% completed
Cumulative payments to Date	Rs.30Mn
Consultancy fees obtained to date	Rs. 0. 15Mn


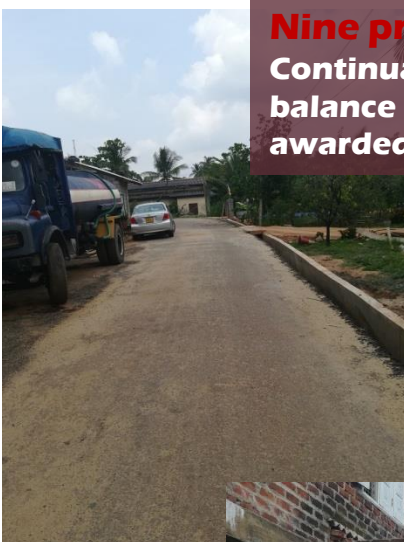




**Nine provinces-
Continuation of
balance of the
awarded contract)**



Consultancy fees expected
Rs. 0.21 Mn


SERVICE ROAD DEVELOPMENT –NOCHCHIYAGAMA

Client	Nochchiyagama PS	  <p>Nine provinces- Continuation of balance of the awarded contract)</p>
Contract sum	Rs.40 Mn	
Source of Fund	Ministry of Mega Police and Western Development	
Commencement date	July 2017	
Completion Date	April 2018	
Allocation for year 2018	Rs.51.9Mn	 
Progress of the Project	25 % Completed <ul style="list-style-type: none"> ▪Road clearance is in progress ▪Construction of drain is in progress 	
Cumulative payments to Date	-	
Consultancy fees obtained to date	-	Consultancy fees expected Rs. 0.2 Mn

UDA 1000 Projects

ON GOING PROJECTS AT ANURADHAPURA DISTRICT**RECREATIONAL FACILITY DEVELOPMENT AT KUMBICHCHANKULAMA,
- JOGGING TRACK, Balance work of Recreational building**

Client	Anuradhapura MC
Contract sum	Rs.52Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date	June2017
Completion Date	March 2018
Allocation for year 2018	Rs.14.8Mn
Progress of the Project	95% Completed 1.2 Km completed. (CECB) Curbs works and bridges to be done (Ranjith constructions)
Cumulative payments to Date	Rs.45Mn
Consultancy fees obtained to date	-Rs. 0.22 Mn

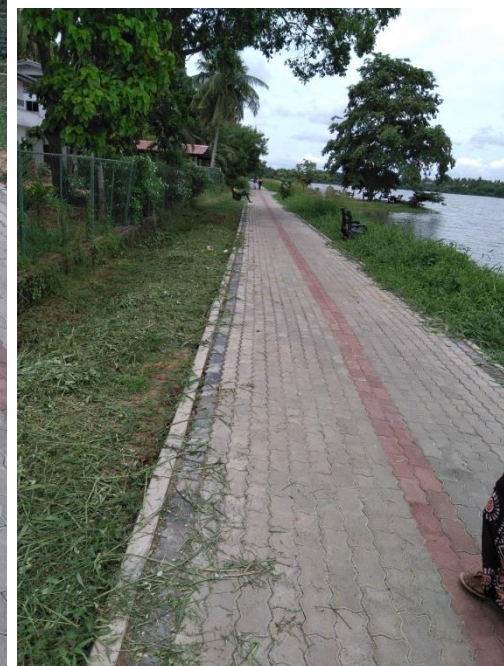




**Consultancy fees expected
Rs. 0.26 Mn**




ON GOING PROJECTS AT ANURADHAPURA DISTRICT**Proposed Access road, parking facilities development at market building at Kekirawa**

Client	Kekirawa P/S	
Contract sum	Rs.52Mn	
Source of Fund	UDA	
Commencement date	April 2017	
Completion Date	September 2017	
Allocation for year 2018	Rs.21.5 Mn	
Progress of the Project	78% Completed Acess road and drains completed . Parking area up to interlocking finishing level	
Cumulative payments to Date	Rs.12Mn	
Consultancy fees obtained to date	--	
Consultancy fees expected Rs. 9.5 Mn		

ON GOING PROJECTS AT ANURADHAPURA DISTRICT**Proposed Commercial Building at Mihinthale**

Client	Mihinthale P/S	 
Contract sum	Rs.28 Mn	
Source of Fund	UDA	
Commencement date	April 2017	
Completion Date	September 2017	
Allocation for year 2018	Rs.14.8Mn	
Progress of the Project	95% Completed 1.2 Km completed. (CECB) Curbs works and bridges to be done (Ranjith constructions)	
Cumulative payments to Date	Rs.45Mn	
Consultancy fees obtained to date	-Rs. 0.22 Mn	Consultancy fees expected Rs. 0.26 Mn

ON GOING PROJECTS AT ANURADHAPURA DISTRICT**ANURADHAPURA TOWN CENTER REDEVELOPMENT PROJECT-PHASE 1
-CONSTRUCTION OF ARCHEOLOGICAL QUARTERS**

Client	UDA	  
Contract sum	Rs.105Mn	
Source of Fund	UDA	
Commencement date	January 2016	
Completion Date	May 2018	
Allocation for year 2018	-	
Progress of the Project	97% Completed <ul style="list-style-type: none">▪Construction 95% completed▪Extra work and Landscaping is in progress	
Cumulative payments to Date	Rs. 87Mn	
Consultancy fees obtained to date	-	Consultancy fees expected -


Nine Province

–New Phase of the Already Started

Construction of Market Building at Kekirawa– STAGE 11

Client	Municipal Council –A/ Pura
Contract sum	Rs.85 Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date	TOR Submitted to CECB. Design doesn't awarded.
Completion Date	December 2018
Allocation for year 2018	Rs.85 Mn
Progress of the Project	Design work is going on.
Cumulative payments to Date	-
Consultancy fees obtained to date	-


Nine provinces-
New Phase of Already
Started Project.

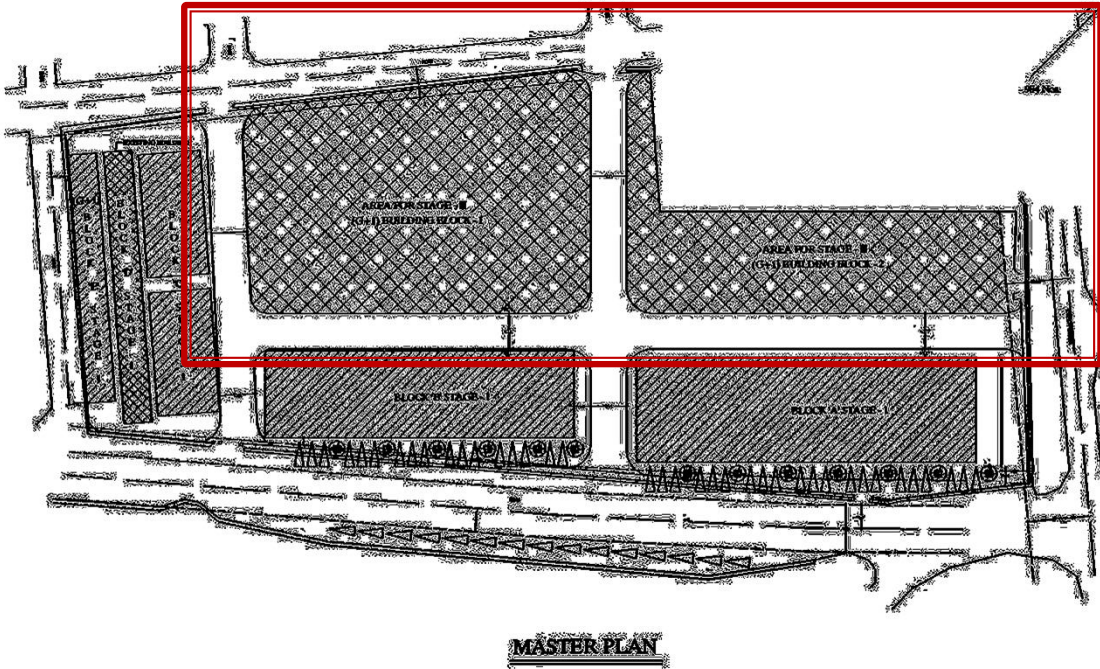

Consultancy fees expected
-

Recreational Facilities development Project at Kumbichchankulama (sisila Uyana)
Stage 111 –Jogging Track Continuation

Client	Municipal Council –A/Pura
Contract sum	Rs.20 Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date	Tender procedure is going on.
Completion Date	December 2018
Allocation for year 2018	Rs.20 Mn
Progress of the Project	Design work is going on.
Cumulative payments to Date	-
Consultancy fees obtained to date	-

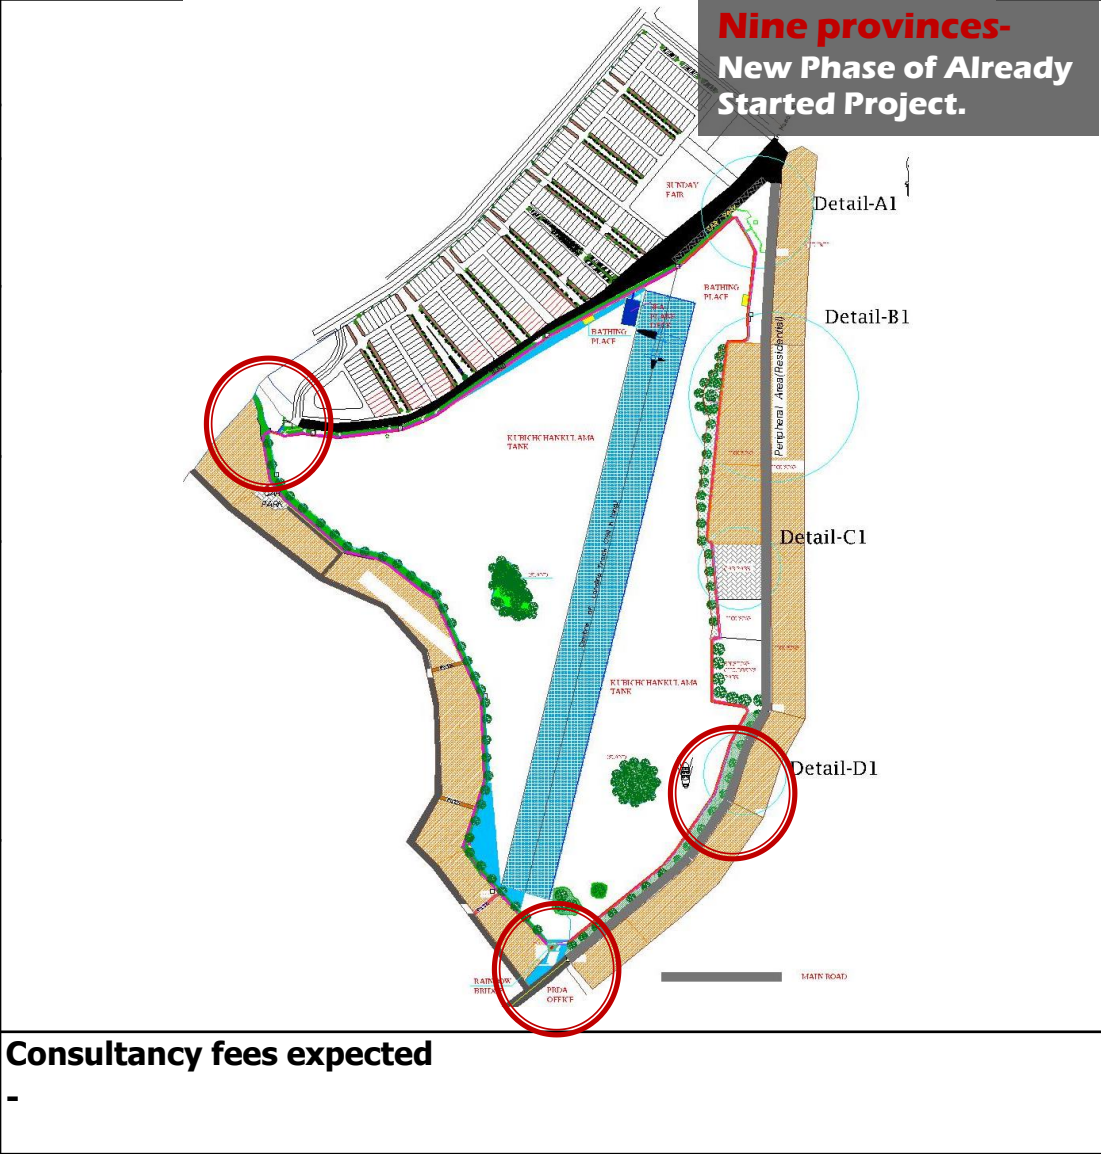


ON GOING PROJECTS AT ANURADHAPURA DISTRICT

Remaiding Defects of Market building at Kekirawa

Client	Kekirawa P/S
Contract sum	Rs.46 Mn
Source of Fund	Ministry of Mega Police and Western Development
Commencement date	January 2018
Completion Date	December 2018
Allocation for year 2018	15 Mn
Progress of the Project	Preparation of estimate for identified defects.
Cumulative payments to Date	Rs. 87Mn
Consultancy fees obtained to date	-

**Nine provinces-
New Phase of Already
Started Project.**

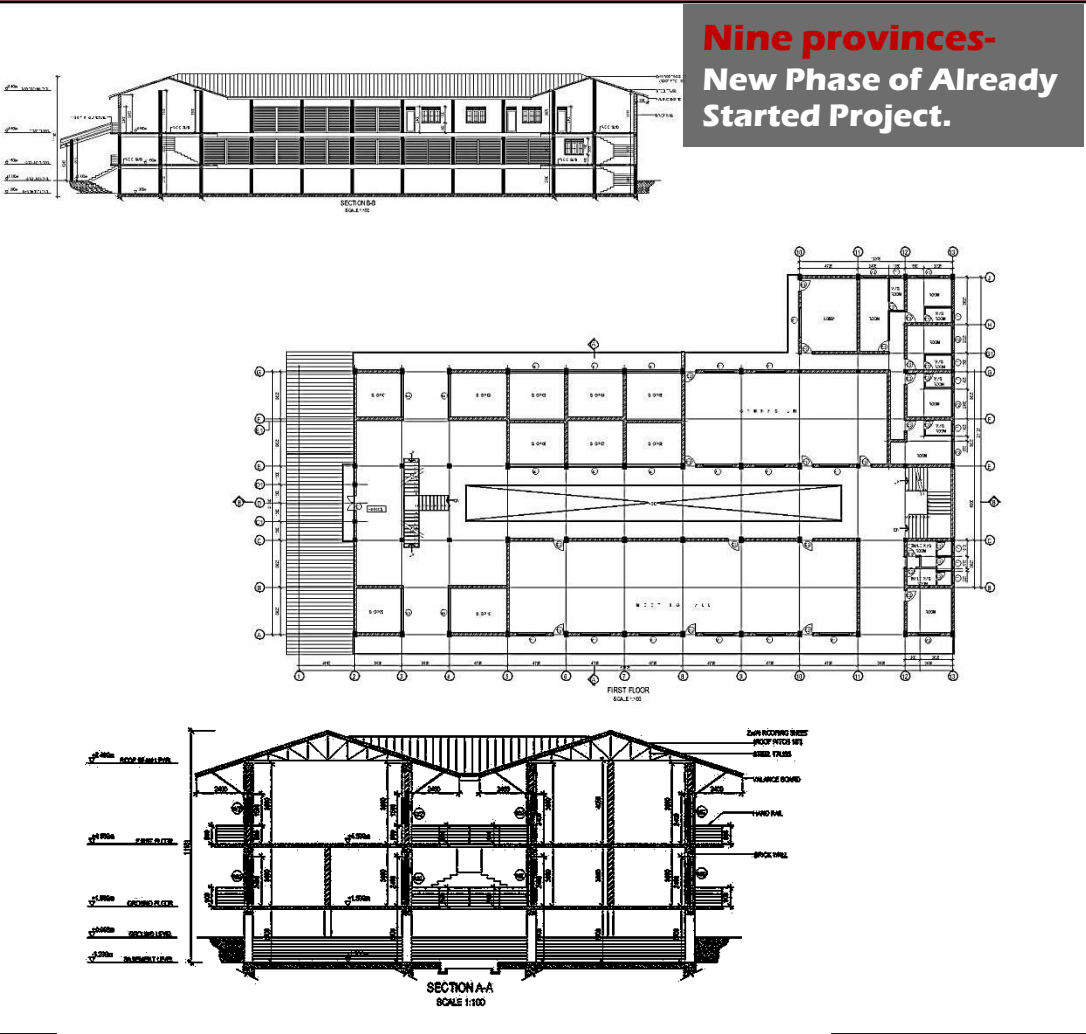

Consultancy fees expected	-
---------------------------	---
